COMECER
an company

Biont-Shielded isolator

O2103011_TP_000-R4.mpp

ID	Task Name	Duration
1	**Shielded isolator with integrated work-related cleaning with radioactivity material_BIONT - Date of conclusion of the contract: 16/09/2022**	**200 days**
2	Order receiving and internal transfer meeting	5 days
3	**ENGINEERING**	**30 days**
4	**Design & documentation**	**30 days**
5	Design	25 days
6	Documentation Phase	1 wk
7	**MANUFACTURING PHASE**	**134 days**
8	Starting production	5 days
9	Material order	3 days
10	Other Commercial /Mechanical/Fabr. Parts	8 wks
11	Frame	8 wks
12	**Stainless Steel Production**	**60 days**
13	Cutting	10 days
14	Bending	5 days
15	Welding	7 wks
16	Hot Cells Assembly	8 wks
17	Start up	3 wks
18	Pre-FAT	8 days
19	**FAT**	3 days
20	**Packaging, Transport**	**7 days**
21	Packaging	6 days
22	Transport, Delivery	3 edays
23	Installation	10 days
24	SAT / Commissioning / Staff Training	3 days
25	IQ/OQ (hot Cell)	4 days
26	IQ/OQ, Hot Tests (Dispenser)	4 days

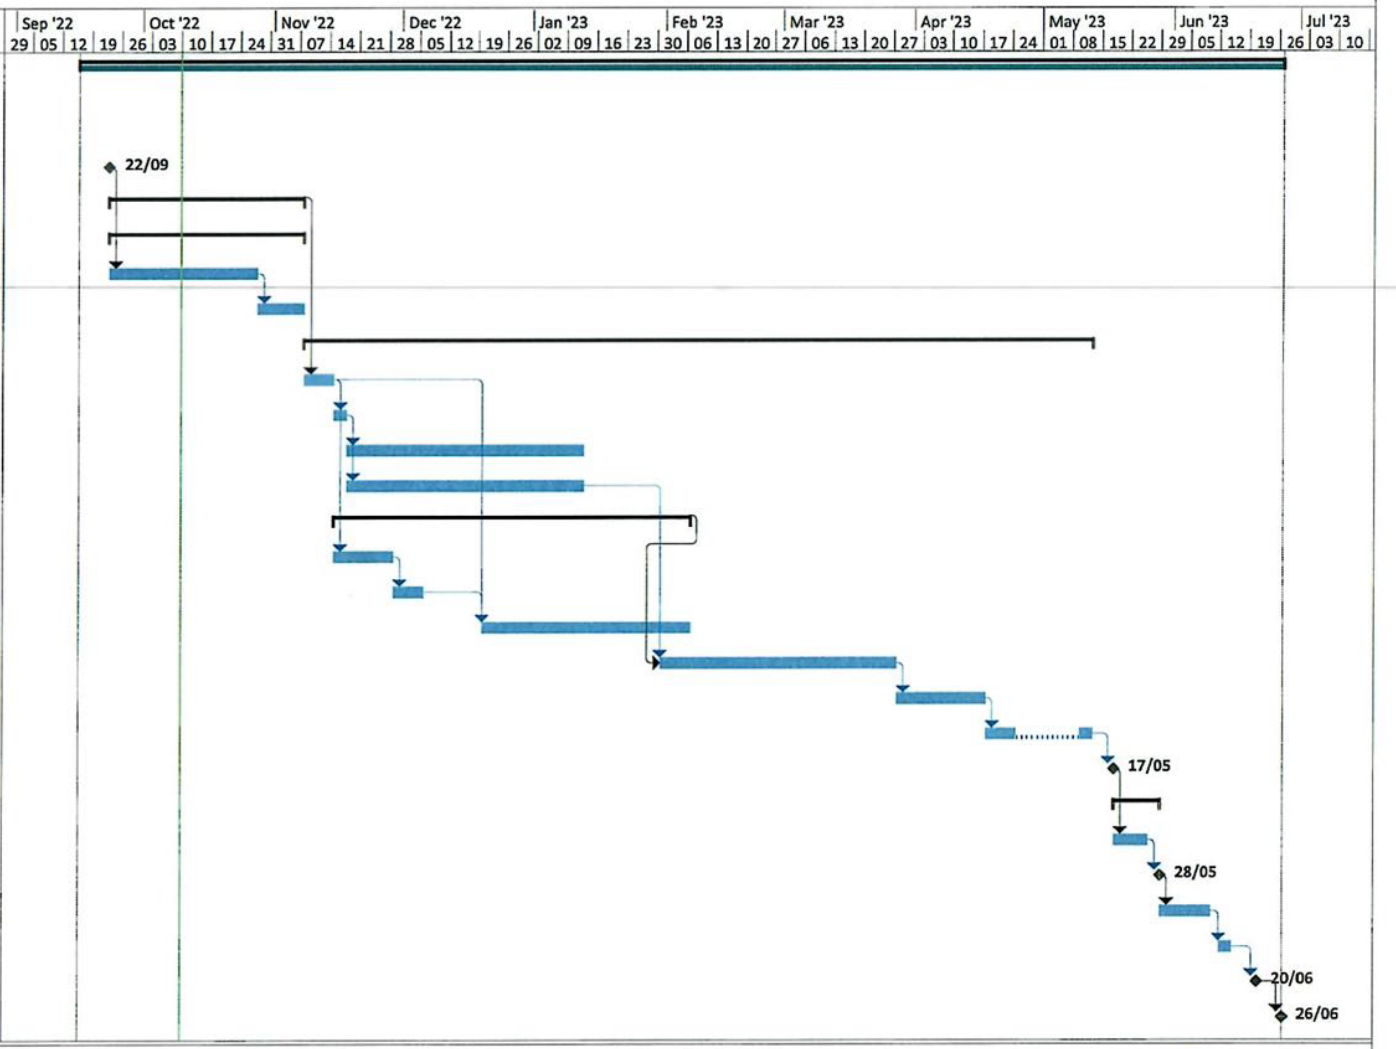

Project: Biont-Shielded isolator
Date: Mon 10/10/22

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only		Manual Progress	
Summary		Inactive Task		Duration-only		Finish-only			
